

Original / Duplicate / Triplicate
CONTRACT CERTIFICATE

(For Other Works)

Date.....20.....

Final Bill

Yelahanka Projects Division,

Received No.....Dated.....Cash Book Voucher No.....dated.....

Scheduled Docket No.....

Name of Work: Providing Kannada words/Alphabets and Sculptures in the premises of Allalasandra and Yelahanka lake in Yelahanka Assembly Constituency

Job Code No: 001-20-000016

Est. cost: 500.00 lakhs

Name of Contractor and Full Address : Sri N. Purushotham Raju (NPR Infra), SLV Nilaya, 38/1, Sankaranthi Layout, 4th main, JP Nagar 7th Phase, Bangalore 560078.

Work Order No EE(Project)/Ynk/Zone/WO/08/2021-22

Dated 16-07-2021

Certified that the measurements were taken by me on 30/6/22.....and recorded in pages 422070 to 422090 of measurement book No.....and that the work is satisfactorily executed.

Contractor

Officer-in-charge of work

Certified that the measurements were taken by me on 30/6/22.....and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account II have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of an imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

If Memorandum of Payment

- 1) Total value of work done or supplies made as per account within
- 2) Deduct amount to be held in reserve being.....percent Rs.....
- 3) Deduct amount to be held in Balance
- 4) Deduct Payment :
 - a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D No.....
 - b) Payments cost store or other materials supplied.Now made recovery of amount creditable to this/other work
Amount paid on this bill Cheque/Cash
- 5) Balance being unpaid value of work done held in reserve
- 6) Deduct cash advance made on the office Cash Book Voucher No.....date less adjustments
- 7) Net amount due to or from contractor
- Unadjusted items
- 8) Advance to contractor for materials brought to site (as detailed) within value of Government materials supplied

Asst. Executive Engineer
Sub-Division Officer

Project Division
Yelahanka Zone

BBMP Bangalore - 83
13765500 - 00
275400 - 00
122950 - 00
122950 - 00
50500 - 00
13800 - 00
137700 - 00
723300 - 00
13042200 - 00

Contractor's Signature

Received Rs.....(in words)

By Cash and by adjustment of Payment as per memorandum.

Witnesses :

1. for NPR INFRATECH

2. for NPR INFRATECH

Dated.....Signature of Contractor

Paid by me by cheque No.....Dated.....

Cash Rs.....Dated.....

Initials of Officer Making Payment

for NPR INFRATECH

(For use in the Office)

Proprietor

Head of Account.....

Audited & admitted for Rs.....

13042200 - 00

by Cheque
and Rs. 723300 - 00 by Adjustment

Asst. Clerk
Project Division
B.B.M.P.

Acct. Sup't.
Project Division
B.B.M.P.

Exec. Engineer
Project Division
B.B.M.P.

BRUHAT BANGALORE MAHANAGARA PALIKE
PROJECT DIVISION YALAHANKA ZONE
Providing Kannada words/Alphabets and Sculptures in the premises of Allalasandra and Yelahanka lake in Yelahanka Assembly Constituency


Abstract

Abstract											
Item No	Description of work	As Per Schedule B			Previous		Present Measurement			Up to Date	
		Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
1	KSRB 2-1.1 : Earthwork in surface excavation in ordinary soil for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeding 50m and lift upto 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled after breaking of clods and neatly dressed as per specifications. specification. No. KBS 2.1(a) / 2.3.1 Note : Adopt item 2.24 for excavation in all types of soils for lowering & levelling the ground for building works by mechanical means KBS Pg No 6, Item No 2.1	799.89	480.70	384505.35	566.36	272248.91	233.53	480.70	112564.43	799.89	184505.35
							233.53		112564.43		384505.35
2	KSRB 2.8 : Providing and Filling in foundation with granite / trap broken metal 100 mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. complete as per specifications. Specification No. KBS Pg No 7, Item No 2.15 (PWD SR 2018-2019)	63.75	2600.49	165786.27	62.60	162790.51	1.15	2600.49	2995.76	63.75	165786.27
									2995.76		
3	KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix 1:4:8(M7.5)with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4-1.3, 4.3 Pg No.13 Item No 4.3	119.79	5462.20	654333.60	86.19	470787.12	33.60	5462.20	183546.48	119.79	654333.60
4	KSRB 4.2.2 : Providing and laying in position reinforced cement concrete of Design mix M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.460 cum, with super plasticisers @ 3 liters confirming to is 9103-1999 reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation for footings, pedestals, retaining walls, return walls, walls (any thickness) including attached pilasters, columns, pillars, posts, struts, buttresses, bed blocks, anchor blocks & plinths etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1, 4.6, Pg No. 14 Item No. 4.11 (PWD SR 2018-2019)	332.36	6058.53	2013588.33	253.72	1537169.06	78.64	6058.53	476419.26	332.36	2013588.33

ON AND CONSULT

placing in position, lapping and / or welding wherever

5	KSRB 4.9.2: Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. TMT bars Fe 500 Specification No KBS 4.46.2, Pg No. 18 Item No. 4.46.2	tonne	34.39	75976.20	2612821.50	23.42	1779962.59	10.97	75976.20	833458.91	34.39	2612821.50
6	KSRB 4.6.9: Providing and removing centering, shuttering, strutting, propping etc., Removal of form Work etc., for edges of slabs and breaks in floors including cost of all materials,labour complete as per specifications. Specifications No. KBS 4.6.9, Pg No 17,Item No 4.36	sqm	0.00	488.23	0.00	0.00	0.00	0.00	488.23	0.00	0.00	0.00
7	KSRB 4.6.9: Providing and removing centering, shuttering, strutting, propping etc., Removal of form Work etc., for edges of slabs and breaks in floors including cost of all materials,labour complete as per specifications. Specifications No. KBS 4.6.9, Pg No 17,Item No 4.36	sqm	1209.68	808.30	977766.36	839.15	678287.46	370.53	808.30	294498.89	1209.68	977766.36
8	KSRB 6.2.3: Providing and constructing burnt brick masonry with approved quality of non-modular bricks of standard size of class designation 5.0Newton per sqmm (table moulded) with cement mortar 1:6 for basement and superstructure / re including cost of materials, labour charges, scaffolding, curing complete as per specifications. Specification No. KBS 6.2, page no.29,item no 6.2 PWD Sr 2018-19	cum	5.39	7183.12	38717.02	5.39	38717.02	0.00	7183.12	0.00	5.39	38717.02
9	KSRB 14.47.3: Providing and laying flooring using prepolished, water cut/gang saw 19mm thick granite laid over bed of 20mm thick 1:4 cm & jointed with neat cement slurry mixed with pigment to match shade of granite slabs including laying POP on finished surface and cleaning the surface, including the cost of all materials and labours etc., complete as per specifications. - using 10mm thick silver grey granite / Multy Red / Ruby Red/ Black / Hassan Green Granite tiles KBS No.14.47.3, Pg No. 110 Item No. 14.47.3	sqm	186.27	1498.84	279188.93	186.27	279188.93	0.00	1498.84	0.00	186.27	279188.93
10	14.55, Providing full nosing for 20 mm thick granite slab using required machinery including cost and conveyance of all materials, labour for all items of work, HOM of equipment etc., complete as per specification KBS No.14.55, Pg No. 111	m	196.45	289.06	56786.23	196.45	56786.23	0.00	289.06	0.00	196.45	56786.23

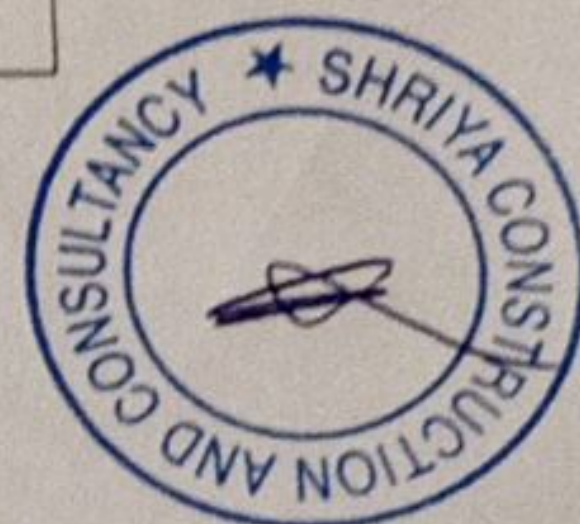


Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
11	Providing and fixing Stainless steel staircase railing as per Chief Architect Drawing No. 11520/ HRSC with hand rail 50mm dia 16 gauge hollow pipe welded to vertical hollow 50mm dia pipe of 16 gauge, stainless steel vertical pipe spaced at 1.20m regular intervals, and 5 Nos of 25mm dia. Stainless steel hollow horizontal pipe are welded to vertical 50mm dia hollow pipe. The entire assembly is fixed to staircase concrete by using expansion bolts by drilling concrete etc., complete including cost of materials, labour, HOM of machineries and electrical charges, etc., complete as per specifications, Pg No. 45 Item No. 4.6 PWD SR 2018-2019)	sqm	18.20	5757.69	104789.90	18.20	104789.90	0.00	5757.69	0.00	18.20	104789.90
12	KSRB 2.11 : Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with lead up to 50 m. and lift up to 1.5 m. including cost of all labour complete as per specifications. specification No. KBS 2.9. (P.NO-7, I.NO-2.10 OF PWD SR 2018-2019	cum	352.58	215.19	75871.90	352.58	75871.90	0.00	215.19	0.00	352.58	75871.90
13	Conveying the excavated earth, debris etc., with all lead and lifts including loading and unloading charges etc., complete as per the direction of the Engineer-in-charge. Pg No 136, Item No17.4	cum	806.91	66.66	53788.62	806.91	53788.62	0.00	66.66	0.00	806.91	53788.62
14	KSRB 5-14.1: Providing and constructing load bearing wall with solid concrete blocks of size 400X200X200mm having block density not less than 1800kg/ m3 having a minimum average compressive strength 5.00N/ mm2 confirming to IS 2185 (part 1) :2005 and constructed with cement mortar 1:4,as per IS 2572-2005 including cost of materials, labour charges, scaffolding, curing, hire charges of machineries etc., complete as per specifications. KBS No.5.4, Pg No. 27 Item No. 5.27.1	cum	298.13	976.39	291090.32	298.13	291090.32	0.00	976.39	0.00	298.13	291090.32
15	KSRB15-1.5 : Providing rough cement plastering 15 mm thick in single coat with cement mortar 1:4, to brick masonry for base of dadoing works with sand of approved quality, providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. KBS No.15.1.5 Pg No. 115 Item No. 15.6	sqm	247.94	221.61	54947.02	247.94	54947.02	0.00	221.61	0.00	247.94	54947.02
16	KSRB: 15-6 : Providing floating coat of cement to plastering and finishing smooth, including cost of materials, labour, curing complete as per specifications. KBS No.15.6, Pg No. 117 Item No. 15.32	sqm	0.00	20.34	0.00	0.00	0.00	0.00	20.34	0.00	0.00	0.00
17	KSRB 15-53.2 Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, curing complete as per specifications. - with primer	sqm	0.00	109.20	0.00	0.00	0.00	0.00	109.20	0.00	0.00	0.00

As Per Schedule B

Previous Present Measurement Up to Date

Qty Amount Qty Amount Qty Amount

Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount	Amount
18	KSRB 9-7.2 : Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 30mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries complete as per specifications. (excluding cost of fixtures) Specification No. KBS 9.34, KPWD SOR 2016-17, SI No 9.22, Page no 54	sqm	0.00	4589.44	0.00	0.00	0.00	0.00	4589.44	0.00	0.00	0.00	0.00
19	KSP providing vitrified tiles 60 x 60cms of approved make, shade and size for flooring laid on a bed of 12mm thick cement mortar 1:3 mix, flush pointing with white cement using colour pigment, including cost of materials, labour, curing complete as per specification. (P.No:109, I.No:14.45 PWD SR 2018-2019)	sqm	144.47	1045.35	151021.71	144.47	151021.71	0.00	1045.35	0.00	144.47	151021.71	
20	Point wiring using copper wire without switch (Class A material). Supplying and wiring adopting loop system in existing PVC conduit/casing capping using 2X1.5Sqmm(phase & Neutral) & 1X1.0 Sqmm (Earth Wire) FRLS multistrand PVC insulated 2x1.5sqmm copper confirming to the GTP With a 6Amps plug type SP control switch shall be fixed on the existing plastic sheet / gand box .the other end of the wire shall be terminated with sufficient loose length in a wood/PVC round block, complete for each outlet. Item 2.1.1a, Item 2.1.2a page No-5, PWD SR 2018-19. short point upto 3m	each	0.00	202.00	0.00	0.00	0.00	0.00	202.00	0.00	0.00	0.00	0.00
21	medium point above 3m- 6m	each	0.00	277.75	0.00	0.00	0.00	0.00	277.75	0.00	0.00	0.00	0.00
22	Concealed Conduit System - Supplying heavy gauge PVC conduit pipe 20/25/32 mm dia 2mm thick conforming to IS 2509 with suitable size bends metal/ pvc junction boxes, adhesive paste etc, and running before concreting and slab. The conduit should be tied to the reinforcement rods by using binding wires and unused ways of junction boxes and pipe ends should be covered using PVC end enclosures, run with 18SWG GI fish wire wherever necessary . item no-1.2, Item 1.2.2, Item 1.2.3 page no-2, PWD SR 2018-19. 25mm dia, 2mm thick	Rmtr	0.00	53.53	0.00	0.00	0.00	0.00	53.53	0.00	0.00	0.00	0.00
23	32mm dia, 2mm thick	Rmtr	0.00	83.83	0.00	0.00	0.00	0.00	83.83	0.00	0.00	0.00	0.00
24	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where ever necessary.. item no-3.4, Item 3.4.1, Item 3.4.2 page no-9, PWD SR 2018-19. 25mm dia, 2mm thick	Rmtr	0.00	54.54	0.00	0.00	0.00	0.00	54.54	0.00	0.00	0.00	0.00
25	32mm dia, 2mm thick	Rmtr	0.00	81.81	0.00	0.00	0.00	0.00	81.81	0.00	0.00	0.00	0.00
26	Supplying and flush modular powder coated / galvanized metal box suitable for mounting modular switch plates. the box should be firm flush mounted after due groove cutting in brick /stone/C.C wall ... item no-1.2, Item 1.2.2, Item 1.2.3 page no-2, PWD SR 2018-19. 1-3 way	each	0.00	95.95	0.00	0.00	0.00	0.00	95.95	0.00	0.00	0.00	0.00
27	4-5 way	each	0.00	106.05	0.00	0.00	0.00	0.00	106.05	0.00	0.00	0.00	0.00

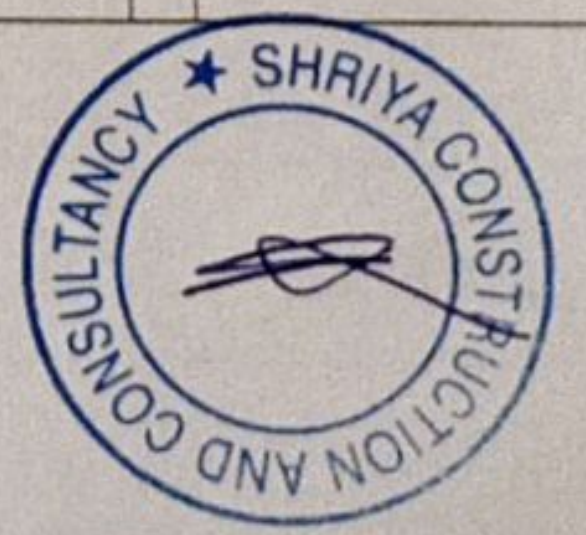

Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
28	Supply and fixing of bakelite D.P / socket/switch with/ without neon indicator over existing wood board or flush mounting in plastic plates/niches as per IS 1293 and IS 3854, Item 1.12, page no-15, PWD SR 2018-19. 16amps combined and socket with indication	nos	0.00	195.94	0.00	0.00	0.00	0.00	195.94	0.00	0.00	0.00
29	electric speed regulator	nos	0.00	151.50	0.00	0.00	0.00	0.00	151.50	0.00	0.00	0.00
30	Supplying and fixing Metal Fan Box with Round Hook item no-2.5.3, Item 2.5.4 page no-3, PWD SR 2018-19.	each	0.00	45.45	0.00	0.00	0.00	0.00	45.45	0.00	0.00	0.00
31	Supplying and fixing Metal Fan Box with Round Hook item no-2.5.3, Item 2.5.4 page no-3, PWD SR 2018-19.	each	0.00	85.85	0.00	0.00	0.00	0.00	85.85	0.00	0.00	0.00
32	Supplying and fixing of Group A, regular MCB distribution boards on wall/woodboard/flush mounting using required clamps, bolts, nuts etc., with provision for fixing suitable type capacity MCB'S single phase/ 3 phase / single door with powder coated painting made out of SWG MS enclosure. item no-5.18, Item 5.18.4 page no-27, 28 PWD SR 2018-19.	NOS	0.00	1222.10	0.00	0.00	0.00	0.00	1222.10	0.00	0.00	0.00
33	Supply and fixing miniature circuit breakers on the existing MCB distribution boards using necessary fixing materials and "C" type curve, Indicator ON/OFF energy cross -3 with as required confirming to IEC 60898 item no-6.16, Item 6.16.3, page no-47, PWD SR 2018-19.	NOS	0.00	918.09	0.00	0.00	0.00	0.00	918.09	0.00	0.00	0.00
34	Supplying of feet - PVC Batten with integrated LED tube W with high quality diffuser with Life of 25000 burning hours & 70% lumen maintenance with CRI > 80. Power Input: 220-240V @ 50/60Hz & Power factor >0.9 along with CE approved. 2 years Warranty against any manufacturing defect working under standard electrical condition. LED light fighting 1 x4'- 20/22 w. item no-12.4.2, Item 7.3.1 page no-69, PWD SR 2018-19 gallery area, room, below gallery area and sitting area	EAC H	0.00	378.75	0.00	0.00	0.00	0.00	378.75	0.00	0.00	0.00
35	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694: confirming to Latest amendments. item no-7.3, Item 7.3.1 page no-46, PWD SR 2018-19. 2.5SQM	Rmtr	0.00	32.32	0.00	0.00	0.00	0.00	32.32	0.00	0.00	0.00
36	Supplying capacitor type ceiling fan complete with down rod blades shackle, canopies etc, for operation on 230 volts, 50 cycles. single phase AC supply conforming to ISS-374-1979 and with double ball bearing system item no-2.5.3, Item 2.5.4 page no-6, PWD SR 2018-19 48" sweep (1200 mm) SR 2018-19.	EAC H	0.00	2110.90	0.00	0.00	0.00	0.00	2110.90	0.00	0.00	0.00
38	16/6 Amps combined plug and socket with control switch item 155 page no-11 SR 2018-19.	NO	0.00	223.41	0.00	0.00	0.00	0.00	223.41	0.00	0.00	0.00
39	Providing and filling sand in excavated trench to cover already laid cable to a depth of 150mm all-round the cable item 6.7, page no- 41 SR 2018-19	mtr	0.00	101.00	0.00	0.00	0.00	0.00	101.00	0.00	0.00	0.00
			As per schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
Description of work												
Item No												

Item No	Description of work	Unit	As Per Schedule B		Previous		Present Measurement		Up to Date	
			Qty	Rate	Amount	Qty	Rate	Amount	Qty	Amount
40	Supply of LED floodlight luminaire with pressure die cast aluminium housing body for optimal thermal dissipation. Lamp compartment comprising of anti glare clear diffuser with Injection moulded polycarbonate/clear glass material, delivering superior light output. Rated life Burning Hrs 50000 hr @ Lumen Maintenance of 70%, CCT > 5500K, IP 66 optical and electrical compartment & impact resistance of complete luminaire > IK08. Power Factor >0.9 with mains, Surge Protection- Min 5KV along with Over voltage/Overload, short circuit/ miss-wiring protection. Compatible for pole mounting with outer dia of 40mm to 50 mm. Universal Voltage driver to operate wide voltage range from 100V to 270V 50/60Hz application. Compliance to IS10322/ IEC 60598, LM 79 & LM 80 Adherence with RoHS. UL approved MCPCB. Top access street light with single screw to ensure ease of maintenance at the sight site location with minimized minimal tools. LED Light fixture with W System Power consumption. LED Efficiency>130lm/w, LED Flood light 120 W (at Theme Statues -2 no.)	EAC H	0.00	6868.00	0.00	0.00	0.00	6868.00	0.00	0.00
41	LED Flood light 150W (around the car Park -6 no's)	EAC H	0.00	8888.00	0.00	0.00	0.00	8888.00	0.00	0.00
42		EAC H	0.00	10352.50	0.00	0.00	0.00	10352.50	0.00	0.00
43	Providing of Hollow Structural Pipe of 600 mm dia with 10 mm hickness for mounting the cars as per directions of Engineer Incharge weighing about 147.63 kgs per Metes with all necessary joints with baseplate and nut bolt system including painting (As per Data Rate including GST)	kg	4089.35	209.78	857851.57	4089.35	0.00	209.78	0.00	4089.35 857851.57
44	Providing of base plate with 10 mm thickness for mounting the cars as per directions of Engineer Incharge about 147.63 kgs per Meter	kg	420.00	151.40	63587.58	420.00	0.00	151.40	0.00	63587.58
45	Providing and Fixing of L= 900 mm Nut with Double bolt of 38 mm dia wieghting 1.0 kg each s per directions of Engineer Incharge (As per Data Rate including GST)	kg	126.00	388.85	48995.10	126.00	0.00	388.85	0.00	48995.10
46	Fixing and Errection of the 600 mm dia MS Column, Cars in vertical levels using the high strength Hydraulic Boomer Vehicles, upto 30 meter height, making hole and fixing with the Nut Bolt for car chasis to Cantilever Plate. High Strength Good Quality Welding of MS Coulmns and Cars Mounting canteer Plate as per IS Standards (1200X1200X10 mm), including all necessary items and errection for complete work and as per Engineer In charge (As per Data Rate including GST)	No	9.00	80548.51	724936.59	9.00	0.00	80548.51	0.00	724936.59
47	Providing and fixing of Guy Rope with Stiffening tixing to MS Columns and Anchored to anchored Pipe with all the necessary hooks, bolts fixtures including all necessary items and errection for complete work and as per Engineer In charge (As per Data Rate including GST)	Rmtr	120.00	1136.25	136350.00	0.00	0.00	1136.25 136350.00	120.00	136350.00
48	Proving and fixing of artistic monumental flower at the top of about 2 meters height with all the necessary joints, hooks, bolts fixtures including all necessary items and errection for complete workand as per Engineer In charge (As per Data Rate including GST)	No	0.00	69558.70	0.00	0.00	0.00	69558.70	0.00	0.00



Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date		
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount	Qty	Amount
49	KSRB 4-6.9 : Providing and placing the ornamental colourful pebbles all round the curve shape inside the VIP Gallery upto 1.2 m height and 0.5 m width and also with Fabricating with 5 mm dia encasement with 20 mm spacing with all necessary L Angles (As per Data Rate including GST)	mtr	0.00	4814.67	0.00	0.00	0.00	0.00	4814.67	0.00	0.00	0.00	0.00	0.00
50	Providing and fixing the vertical Coulumn with Base base plate at Top and bottom with proper Welding and also welded as shown in the drawing/ as directed by Engineer in Charge consisting of M.S Steel tubes for vertical - 2"X 2"- 4 no's (2 feet X 2 feet Size)-vertical-MS Steel Tubes, 2" X 2"-4no's (2 feet X 2 feet Size)-horizontal, 1.5"X0.75"- MS Steel Tubes no's (inclined 2.5")-horizontal with complete necessary items as per IS codes, including painting with iron gutter with PVC fittings draing out the water (As per Data Rate including GST) 2"X 2"- 4 no's (2 feet X 2 feet Size)-complete (L)	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
51	2" X 2"-4no's (2 feet X 2 feet Size)-horizontal	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
52	1.5"X0.75"- 4no's (inclined 2.5")-inclined 5x4x2	mtr	0.00	308.05	0.00	0.00	0.00	0.00	308.05	0.00	0.00	0.00	0.00	0.00
53	Providing and fixing the of roof truss with proper Welding and also welded as shown in the drawing/ as directed by Engineer in Charge consisting of 2"X 2"-4 no's (2 feet X 2 feet Size)-vertical-MS Steel Tubes, 2" X 2"-4no's (2 feet X 2 feet Size)-horizontal, 1.5"X0.75"- 8 no's (inclined 2.5")-horizontal with complete necessary items as per IS codes, including painting (As per Data Rate including GST) 2"X 2"-4 no's (2 feet X 2 feet Size)-complete (L)	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
54	2" X 2"-4no's (2 feet X 2 feet Size)-horizontal	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
55	1.5"X0.75"- 4no's (inclined 2.5")-inclined 5x4x2	mtr	0.00	308.05	0.00	0.00	0.00	0.00	308.05	0.00	0.00	0.00	0.00	0.00
56	Providing and fixing the support in between trusses with proper Welding and also welded as shown in the drawing/ as directed by Engineer in Charge consisting of 2"X2"-4no's (2 feetX 2 feet Size)-vertical-, 2"X2"- vertical no's (2 feetX 2 feet Size)-horizontal with complete necessary items as per IS codes , including painting (As per Data Rate including GST) 2"X2"-4no's (2 feetX 2 feet Size)-vertical-	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
57	2"X2"-vertical no's (2 feetX 2 feet Size)-horizontal	mtr	0.00	398.95	0.00	0.00	0.00	0.00	398.95	0.00	0.00	0.00	0.00	0.00
58	Providing and fixing the perlin's Welding and also welded as shown in the drawing/ as directed by Engineer in Charge consisting of 1.5" X 0.75" with complete necessary items as per IS codes , including painting (As per Data Rate including GST) 1.5"X0.75"	mtr	0.00	222.20	0.00	0.00	0.00	0.00	222.20	0.00	0.00	0.00	0.00	0.00
59	Supplying and fixing new Mangalore tiles on existing reepers including cost of materials, labour, HOM complete as per specifications. Item no.37.9 Page no. PWD SR-2018-19	sqm	158.18	435.71	68919.06	0.00	0.00	158.18	435.71	68919.06	158.18	68919.06	158.18	68919.06

As Per Schedule B			Previous			Present Measurement			Up to Date		
Unit	Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount	Amount



Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
60	KSRB 15-16.1 Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications. - with primer	sqm	0.00	109.20	0.00	0.00	0.00	0.00	109.20	0.00	0.00	0.00
61	KSRB 2-2.1-Earthwork excavation for foundation buildings, water supply, sanitary lines & electrical of conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50m. after breaking of clods complete as per specifications. Specification No. KBS 2.1(a)/2.3.5 item no 2.3, page no-6 PWD sr 2018-19	cum	0.00	326.15	0.00	0.00	0.00	0.00	326.15	0.00	0.00	0.00
62	KSRB 2.8 : Providing and Filling in foundation with granite / trap broken metal 100 mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. complete as per specifications. Specification No. KBS Pg No 7, Item No 2.1	cum	0.00	2502.36	0.00	0.00	0.00	0.00	2502.36	0.00	0.00	0.00
63	KSRB 4-1.2: Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40 mm and down size graded granite metal coarse aggregates @ 0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15cms. Thick, well compacted, in foundation including cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2 item no-4.2, page no-13, PWD sr 2018-19.	cum	29.88	5665.62	169309.54	7.39	41868.90	22.49	5665.62	127440.65	29.88	169309.54
64	KSRB 5.3-3 Providing and constructing granite/ trap/ basalt size stone masonry in basement with cement mortar 1:6, edges of stones chistle dressed in courses not less than 15cms high, bond stones at two m. apart in each course including cost of materials, labour, scaffolding, curing complete as per specifications. K.B.S 5.1.13 item no-5.9, page no-25, PWD sr 2018-19.	cum	130.82	5931.77	775976.41	8.96	53148.66	121.86	5931.77	722827.75	130.82	775976.41




Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount	
65	KSRB 4.2.2: Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 320kgs, with 20mm and down sizegraded granite metal coarse aggregates @ 0.69cum and fine aggregates @ 0.460cum, with super plasticiser @ 3lts confirming to IS: 9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick,vibrated for all works in foundation for footings, pestastals, retaining walls, return walls, walls (any thickness) including attached pilasters, columns/pillars, posts, struts, buttresses, bed blocks, anchor blocks, and plinths etc., including cost of all materials, labour, HOM of machinery, curing, complete as per specifications. Specification No. KBS 4.1.4.6 item no-4.11, page no-14, PWD sr 2018-19.	cum	0.00	6172.84	0.00	0.00	0.00	0.00	6172.84	0.00	0.00	0.00	
66	KSRB 2.3: Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. In depth, compacting each deposited layer by ramming after watering with lead upto 50 m. & lift upto 1.5m including cost of all labour complete as per specifications. Specification No K.B.S. 2.9 item no-2.10, page no-7, PWD sr 2018-19.	cum	0.00	219.25	0.00	0.00	0.00	0.00	219.25	0.00	0.00	0.00	
67	KSRB 6-2.3 : Providing and constructing burnt brick masonry with approved quality of non-modular bricks of standard size of class designation 5.0Newton per sqmm (table moulded) with cement mortar 1:6 for basement and superstructu/re including cost of materials, labour charges, scaffolding, curing complete as per specifications. Specification No. KBS 6.2, page no.29,item no 6.2 PWD Sr 2018-19	cum	0.00	7318.18	0.00	0.00	0.00	0.00	7318.18	0.00	0.00	0.00	
68	KSRB 4.9.2 Providing T M T steel reinforcement for R.C.C work including straightening ,cutting, bending, hooking, placing in position, lapping and /or welding wherever required, tying with binding wire, anchoring to the adjoining members wherever necessary, as per designs (laps, hooks and wastage shall not be measured and paid) including cost of all materials, labour, HOM of machineries etc., complete as per specifications. Specification No KBS 4.6.3. TMT bars Fe 500 item no-4.46.2, page no-18, PWD sr 2018-19.	tonne	0.00	77409.71	0.00	0.00	0.00	0.00	77409.71	0.00	0.00	0.00	
69	KSRB 4-6.5: Providing & removing centering, shuttering, strutting, propping etc., and removal of form work for flat surface such as suspended floors, roofs, landings, balconies and likes, thickness upto 200mm including cost of all materials , labour complete as per specifications item no-4.32, page no-16, PWD sr 2018-19	sqm	0.00	497.40	0.00	0.00	0.00	0.00	497.40	0.00	0.00	0.00	



Item No	Description of work	Unit		Qty		Amount		Rate		Qty		Amount		Rate		Qty		Amount	
	KSRB 9-7.1: Providing & fixing in position fully																		

Item No	Description of work	Unit	Qty	Rate	Amount	Qty	Rate	Amount	Qty	Rate	Amount
70	KSRB 9-7.1: Providing & fixing in position fully panelled Mathi/Nandi wood shutters for doors, styles and rails of 30mm thick with bottom & lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25 mm thick of exterior grade plain particle board including cost of materials, labour, HOM of machineries complete as per specifications (excluding cost of fixtures). Specification No K.B.S.9.34 item no-9.20, page no-54, PWD sr 2018-19.	sqm	0.00	4163.58	0.00	0.00	4163.58	0.00	0.00	0.00	0.00
71	KSRB 9-16.3: Providing & fixing in position Mathi/Nandi wood fully panelled shutters for windows with styles and rails of 35mm thick, 75mm wide in two halves with panels of 25mm thick including cost of materials, labour charges, HOM of machineries complete as per specifications (excluding cost of fixtures) item no-9.45, page no-56, PWD sr 2018-19.	sqm	0.00	4739.53	0.00	0.00	4739.53	0.00	0.00	0.00	0.00
72	KSRB 15-3.8: Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering : providing and removing scaffolding, including cost of materials, labour, curing complete as per specification item no-15.16, page no-116, PWD sr 2018-19.	sqm	216.37	284.70	61600.28	153.28	43638.63	63.09	17961.65	216.37	61600.28
73	KSRB 14.10-1: Flooring with 25mm to 40mm thick polished tandur blue stone slabs using cement mortar 1:6, 25 mm thick over existing cement concrete bed or top of roof laid to line and level and jointed with cement slurry mixed with pigment to match the shade of the slab, including cost of materials,labour,curing, polishing complete as per specifications. item no-14.15, page no-105, PWD SR 2018-19.	sqm	0.00	1367.86	0.00	0.00	1367.86	0.00	0.00	0.00	0.00
74	KSRB 15.10.3 Providing white washing to new wall surface in two coats with lime of approved quality, to give an even shade including cost of materials, labour as per specifications item no-15.40, page no-117, PWD SR 2018-19.	sqm	0.00	14.18	0.00	0.00	14.18	0.00	0.00	0.00	0.00
75	KSRB 15-13.1 : Providing and applying one coat distemper primer of approved brand on wall surface after thoroughly brooming the surface to removal of all dirt, dust, mortar drops and other foreign matter including preparing the surface, even and sand paper smooth, cost of materials, labour, complete as per specifications item no-15.46 page no-118, PWD SR 2018-19.	sqm	0.00	38.18	0.00	0.00	38.18	0.00	0.00	0.00	0.00
76	KSRB 15-15.1: Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labours, complete as per specifications. item no-15.51, page no-119, PWD SR 2018-19.	sqm	0.00	94.90	0.00	0.00	94.90	0.00	0.00	0.00	0.00

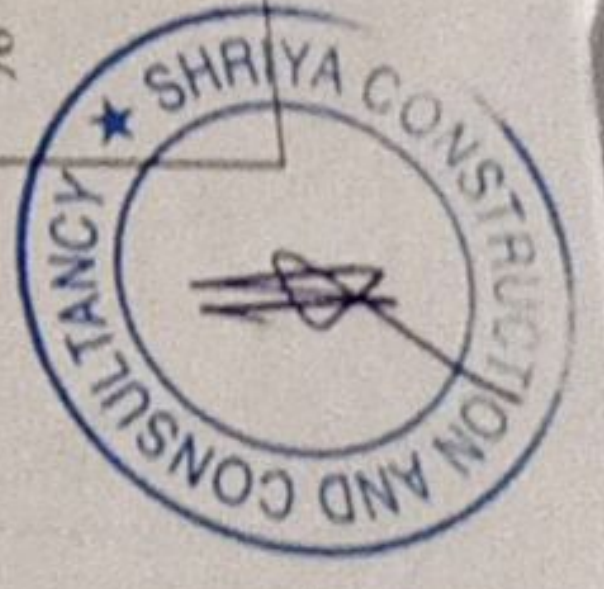

83



Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
90	KSRRB M300- 2.1. Grassing with Doobs grass including watering and maintenance of the lawn for 30 days or more till the grass forms a thick lawn free from weeds and fit for moving including supplying good earth if needed complete as per specifications. MORTH Specification No. 307 ii) In rows 7.5 cm apart in either direction	sqm	162.91	91.00	14824.97	162.91	14824.97	0.00	91.00	0.00	162.91	14824.97
91	Providing and fixing Stainless steel staircase railing as per Chief Architect Drawing No. 11520/ HRSC with hand rail 50mm dia 16 gauge hollow pipe welded to vertical hollow 50mm dia pipe of 16 gauge, stainless steel vertical pipe spaced at 1.20m regular intervals, and 5 Nos of 25mm dia. Stainless steel hollow horizontal pipe are welded to vertical 50mm dia hollow pipe. The entire assembly is fixed to staircase concrete by using expansion bolts by drilling concrete etc., complete including cost of materials, labour, HOM of machineries and electrical charges, etc., complete as per specifications. Pg No. 45 Item No. 7.38	sqm	80.49	6446.08	518845.19	34.88	224775 224839.36	45.61	6446.08	294005.83	80.49	518845.19
92	Providing and laying For elevation using white sadarhalli stone with stone chiesing and fine dressed granite stone slabs 100 mm thick with cement mortar 1:3 including cost of materials, labour, curing complete as per specifications. (AS per Approved Data rate including GST)	sqm	0.00	4898.50	0.00	0.00	0.00	0.00	4898.50	0.00	0.00	0.00
93	KSRB 5.27.1 : Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar 1:6 stone Masonary in superstructure with cement mortar , edge of stones chistle dressed in courses not less than 15 cms high, bond stones at two 2M. apart in each course including cost of materials, labour, curing complete as per specifications. KBS 5.14.1, Pg No 27, Item No 5.27.1	cum	31.33	6192.31	194005.07	31.33	194005.07	0.00	6192.31	0.00	31.33	194005.07
94	Item-no-7.36 Providing and fixing M.S.Grill over existing compound wall as per Chief Architect drawing No. 12686, using 16mm x 16mm M.S.Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S. flat for ornamental design and providing shop edge design at the vertex of every vertical rods, including welding, grinding wherever necessary. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc., complete. The work includes cost of all materials, labour charges for all items of work, hire charges for welding, cutting and grinding equipment, and electricity charges, etc., complete as per specification Item.no7.36, Pg No.44	sqm	0.00	5747.91	0.00	0.00	0.00	0.00	5747.91	0.00	0.00	0.00





Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
95	Item-no-7.36 Providing and fixing M.S.Gate as per chief architect drawing, using 50mm x 50 mm 14 gauge M.S. hollow pipe frame work bent to ornamental shape as shown in the drawing and 35 mm x 6 mm and 16 x 16 mm square rods and verticals alternatively spaced at 4 cms c/c in two halves and 40 mm x 6 mm M.S. flats for horizontal member and at the top cast iron spikes are provided at alternative vertical members as shown in the drawing etc., complete. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc., complete. The work includes cost of all materials, labour charges for all items of work, hire charges for welding, cutting and grinding equipment, and electricity charges, with lead and lift, loading and unloading charges, etc., complete as per specification Item.no 7.37, Pg No.45	sqm	2.25	3224.65	7255.46	0.00	0.00	2.25	3224.65	7255.46	2.25	7255.46
96	KSRRB MS00-5.1. Over head Signs (Truss and Vertical Support): Manufacturing, Supply and installation of retro-reflective Over-Head Gantry signboards made out of cube corner micro prismatic grade sheeting conforming to Type XI standards of IRC:67:2012 fixed over 4mm thick Aluminium Composite Panel sheet, excluding the cost of Type XI retro-reflective sheeting and 4mm Thick ACP sheet with suitable back support frame over a designed support system of aluminum alloy or galvanised steel trestles and trusses of section type as per structural design requirements and approved plans complete as per specifications. Vertical and Lateral Clearance of the Gantry shall be as per IRC 67 2012 and as per Clause 800.2.2 and 800.2.3 and installed as per clause 800.2.7. Pg No. 180 Item No.24.50	No	0.00	75634.86	0.00	0.00	0.00	0.00	75634.86	0.00	0.00	0.00
97	CHEVEROLET FLEET MAST. Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and Length 197.75 width 73.4 height 66.1 in inch total weight with engine 1451 actual weight 870 kg Colour PINK Country CANADA (As per Data Rate including GST)	No	1.00	2070500.00	2070500.00	1.00	2070500.00	0.00	2070500.00	0.00	1.00	2070500.00
98	SRUDEBAKER CHAPION. Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and Length 197.2 width 69.9 height 62.9 in inch total weight with engine 1265 actual weight 759kg Colour Dustbin Blue Country USA (As per Data Rate including GST)	No	1.00	2095750.00	2095750.00	1.00	2095750.00	0.00	2095750.00	0.00	1.00	2095750.00




Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date		
			Qty	Rate	Amount	Qty	Amount		Qty	Rate	Amount	Qty	Amount	
99	JAGUAR 16 SOVEREIGN Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and 195.28 width 69.69 height 54.21 in inch total weight with engine 1720 actual weight 1032 kg Color Yellow Country UK (As per Data Rate including GST)	No	1.00	1717000.00	1717000.00	1.00	1717000.00		0.00	1717000.00	0.00	1.00	1717000.00	
100	DODGE KINGSWAY Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and 189.5 width 73.4 height 63.6 in inch total weight with engine 1395 actual weight 837 kg Color Apollo Green Country USA (As per Data Rate including GST)	No	1.00	1313000.00	1313000.00	1.00	1313000.00		0.00	1313000.00	0.00	1.00	1313000.00	
101	FILLMAN MINOR Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and 165 width 62.8 height 38 in inch total weight with engine 925 actual weight 355 kg Color Brown Country UK (As per Data Rate including GST)	No	1.00	2624000.00	2624000.00	1.00	2624000.00		0.00	2624000.00	0.00	1.00	2624000.00	
102	NOSSAN BLUEBIRD 910 U2 Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lakering, etc, complete and transportation to the site location and 157 width 42 height 61 in inch total weight with engine 990 actual weight 594 kg Color Orange Country Japan (As per Data Rate including GST)	No	1.00	1969500.00	1969500.00	1.00	1969500.00		0.00	1969500.00	0.00	1.00	1969500.00	



No	Description of work	Unit	Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
	NOSSAN BLUEBIRD 910 U2											

Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount		Qty	Rate	Amount	Qty	Amount
103	MORRIS SERIES Z VAN: Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lackering, etc, complete and transportation to the site location and Length 149 width 54.5 height 60 in inch total weight with engine 910 actual weight 546 kg Coulor German RED Country UK (As per Data Rate including GST)	No	1.00	2121000.00	2121000.00	1.00	2121000.00		0.00	2121000.00	0.00	1.00	2121000.00
104	AUSTIN-8: Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lackering, etc, complete and transportation to the site location and Length 149 width 56 height 60 in inch total weight with engine 799 actual weight 479.4 kg Coulor Parot Green Country UK (As per Data Rate including GST)	No	1.00	1616000.00	1616000.00	1.00	1616000.00		0.00	1616000.00	0.00	1.00	1616000.00
105	FIAT TOPOLINO: Providing the outdoor brightly colored popular vintage car models made out of Welded Iron Automobile Parts, Suitable MS, brass casting with necessary steel rods for strengthening, as per the approved theme and sample including preparation of mould and casting with oxidizing, lackering, etc, complete and transportation to the site location and Length 127.8 width 50.15 height in inch 54.21 total weight with engine 550 actual weight 330 kg Coulor PINK Country ITALY (As per Data Rate including GST)	No	1.00	1818000.00	1818000.00	1.00	1818000.00		0.00	1818000.00	0.00	1.00	1818000.00
106	Providing, Fabricating and Fixing of Globe made out of Welded Iron Automobile Parts, materials as per drawings for appearance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge (inclusive of all taxes) Dimesions : 108 x 108 x 108 inches Base size required: (5 x 5 feet) waight: 1.5 Ton approximately (inclusive of all taxes) As per approved quotation	No	1.00	1616000.00	1616000.00	1.00	1616000.00		0.00	1616000.00	0.00	1.00	1616000.00
	Providing, Fabricating and Fixing of Elephant made out of Welded Iron Automobile Parts, materials as per drawings for appearance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge (inclusive of all taxes) Dimesions : 108 x 108 x 108 inches Base size required: (5 x 5 feet) waight: 1.5 Ton approximately (inclusive of all taxes) As per approved quotation	No	1.00	1464500.00	1464500.00	1.00	1464500.00		0.00	1464500.00	0.00	1.00	1464500.00

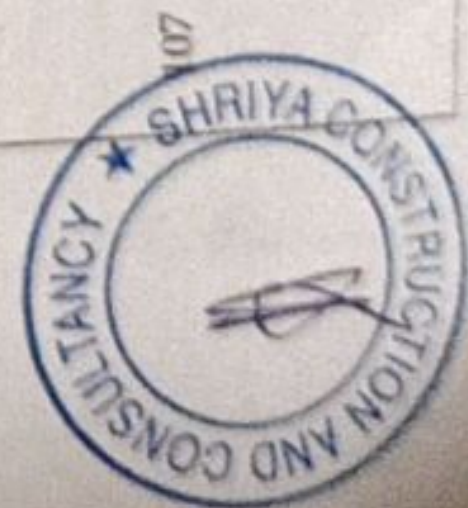

Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount		Qty	Rate	Amount	Qty	Amount
108	Poviding, Fabricating and Fixing of Auto made out of Welded Iron Automobile Parts, materials as per drawings for appereance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge. (inclusive of all taxes) Dimesions : 64 x 102 x 44 inches Base size required: (10.5 x 6 feet) wieght: 1.5 Ton approximately (inclusive of all taxes) As per approved quotation	No	1.00	1616000.00	1616000.00	1.00	1616000.00		0.00	1616000.00	0.00	1.00	1616000.00
109	Poviding, Fabricating and Fixing of Bullock Cart made out of wWelded Iron Automobile Parts, materials as per drawings for appereance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge. (inclusive of all taxes) Dimesions : 42 x 98 x 24 inches Base size required: (8 x 4 feet) Wieght: 350Kgs approximately (inclusive of all taxes) As per approved quotation	No	1.00	808000.00	808000.00	1.00	808000.00		0.00	808000.00	0.00	1.00	808000.00
110	Poviding, Fabricating and Fixing of Boat made out of wWelded Iron Automobile Parts, materials as per drawings for appereance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge. (inclusive of all taxes) Dimesions : 42 x 98 x 24 inches Base size required: (8 x 4 feet) Wieght: 350Kgs approximately (inclusive of all taxes) As per approved quotation	No	1.00	1616000.00	1616000.00	0.00	0.00		1.00	1616000.00	1616000.00	1.00	1616000.00
111	Poviding, Fabricating and Fixing Horse made out of wWelded Iron Automobile Parts, materials as per drawings for appereance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge. (inclusive of all taxes) Dimesions : 42 x 98 x 24 inches Base size required: (8 x 4 feet) Wieght: 350Kgs approximately (inclusive of all taxes) As per approved quotation	No	1.00	1212000.00	1212000.00	1.00	1212000.00		0.00	1212000.00	0.00	1.00	1212000.00
112	Poviding, Fabricating and Fixing Ashoka Pillar made out of wWelded Iron Automobile Parts, materials as per drawings for appereance and dimesions is as indicated in techinal drawings enclosed including cost of all materials, labour, HOMof machinery, complete as per direction of Engineer in Charge. (inclusive of all taxes) Dimesions : 42 x 98 x 24 inches Base size required: (8 x 4 feet) Wieght: 350Kgs approximately (inclusive of all taxes) As per approved quotation	No	1.00	1414000.00	1414000.00	1.00	1414000.00		0.00	1414000.00	0.00	1.00	1414000.00



As Per Schedule B			Previous			Present Measurement			Up to Date	
Unit	Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
Continuation of work										

Item No	Description of work	Unit	As Per Schedule B			Previous			Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount		Qty	Rate	Amount	Qty	Amount
113	Providing, the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 7ft height (Kalia) with unique features as per the approved artistic impression with necessary water proof painting including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)(AS per approved data rate)	No	1.00	386375.50	386375.50	0.00	0.00		1.00	386375.50	386375.50	1.00	386375.50
114	Porviding, the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 5ft height (chota bheem) with unique features as per the approved artistic impression with necessary water proof painting including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes) (AS per approved data rate)	No	1.00	390567.00	390567.00	0.00	0.00		1.00	390567.00	390567.00	1.00	390567.00
115	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Dolu or Daisy Duck) with unique features as per the approved artistic impression with necessary water proof painting including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes) (AS per approved data rate)	No	2.00	390516.50	781033.00	0.00	0.00		2.00	390516.50	781033.00	2.00	781033.00



Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
116	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Bholu or Micky Mouse) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)/(AS per approved data rate)	No	2.00	395869.50	791739.00	0.00	0.00	~~2.00~~	~~395869.50~~	~~791739.00~~	2.00	791739.00
117	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Chutki or Minnie Mouse) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)/(AS per approved data rate)	No	2.00	395314.00	790628.00	0.00	0.00	~~2.00~~	~~395314.00~~	~~790628.00~~	2.00	790628.00
118	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Jaggu) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)/(AS per approved data rate)	No	1.00	393799.00	393799.00	0.00	0.00	~~1.00~~	~~393799.00~~	~~393799.00~~	1.00	393799.00
119	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Raju) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)	No	1.00	391223.50	391223.50	0.00	0.00	~~1.00~~	~~391223.50~~	~~391223.50~~	1.00	391223.50



Item No	Description of work	Unit	As Per Schedule B			Previous		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
120	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 4ft height (Indumathi) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)(AS per approved data rate)	No	1.00	388143.00	388143.00	0.00	0.00	1.00	388143.00	388143.00	1.00	388143.00
121	Providing the Theme Statue made out of rich mix ferro cement with necessary reinforcement with mesh work, as required for stability of statue of size 7ft height (Male Donald Duck) with unique features as per the approved artistic impression with necessary water proof painting finishing including cost of scaffolding foam wok and fixing on a firm platform with necessary base plate and bolts etc complete as per direction of officer in charge (inclusive of all applicable taxes)	No	1.00	384656.50	384656.50	0.00	0.00	1.00	384656.50	384656.50	1.00	384656.50
EIRL-1	Granite Stone pillar 7ftx1ftx1ft including fixing, crane and transportation charges etc., (Approved Data Rate)		6.00	60000.00	360000.00	0.00	0.00	6.00	60000.00	360000.00	6.00	360000.00
EIRL-2	Granite Stone kalsa 2ftx1ftx1ft including fixing and transportation charges etc., (Approved Data Rate)		6.00	10000.00	60000.00	0.00	0.00	6.00	10000.00	60000.00	6.00	60000.00
EIRL-3	Fabricating, providing and erecting in position of MS Hot Dip Galvanised Sq. Hallow Poles of 132 X 132 Heavy gauge of length 3000mm with MS. Hot dip Galvanised grill work as per approved design and drawing of chief architect. Using 12 X 75mm galvanised flat for alround frame and 20 X 20mm galvanised forged design with square for vertical at 150mm c/c as shown in the drawing including providing forged ornamental arrowhead at top and bottom. The work is inclusive of thoroughing flat, square rods, placing welding all the joints, including grinding, finishing 2 coats of anticorrosive paint over one coat of metal primer. The rate is inclusive of all materials like MS. Hollow galvanized pipe, flats, forged square rods, cost of labour for all items of work cost painting, welding, cutting, grinding with all lead and lift as per specification including loading and unloading with cost and conveyance of all materials, labour, machinery and incidental charges for the successful completion of the work as per the direction of the Engineer-in-charge of the work. (Data Rate)		350.10	9144.00	3201314.40	0.00	0.00	350.10	9144.00	3201314.40	350.10	3201314.40



